









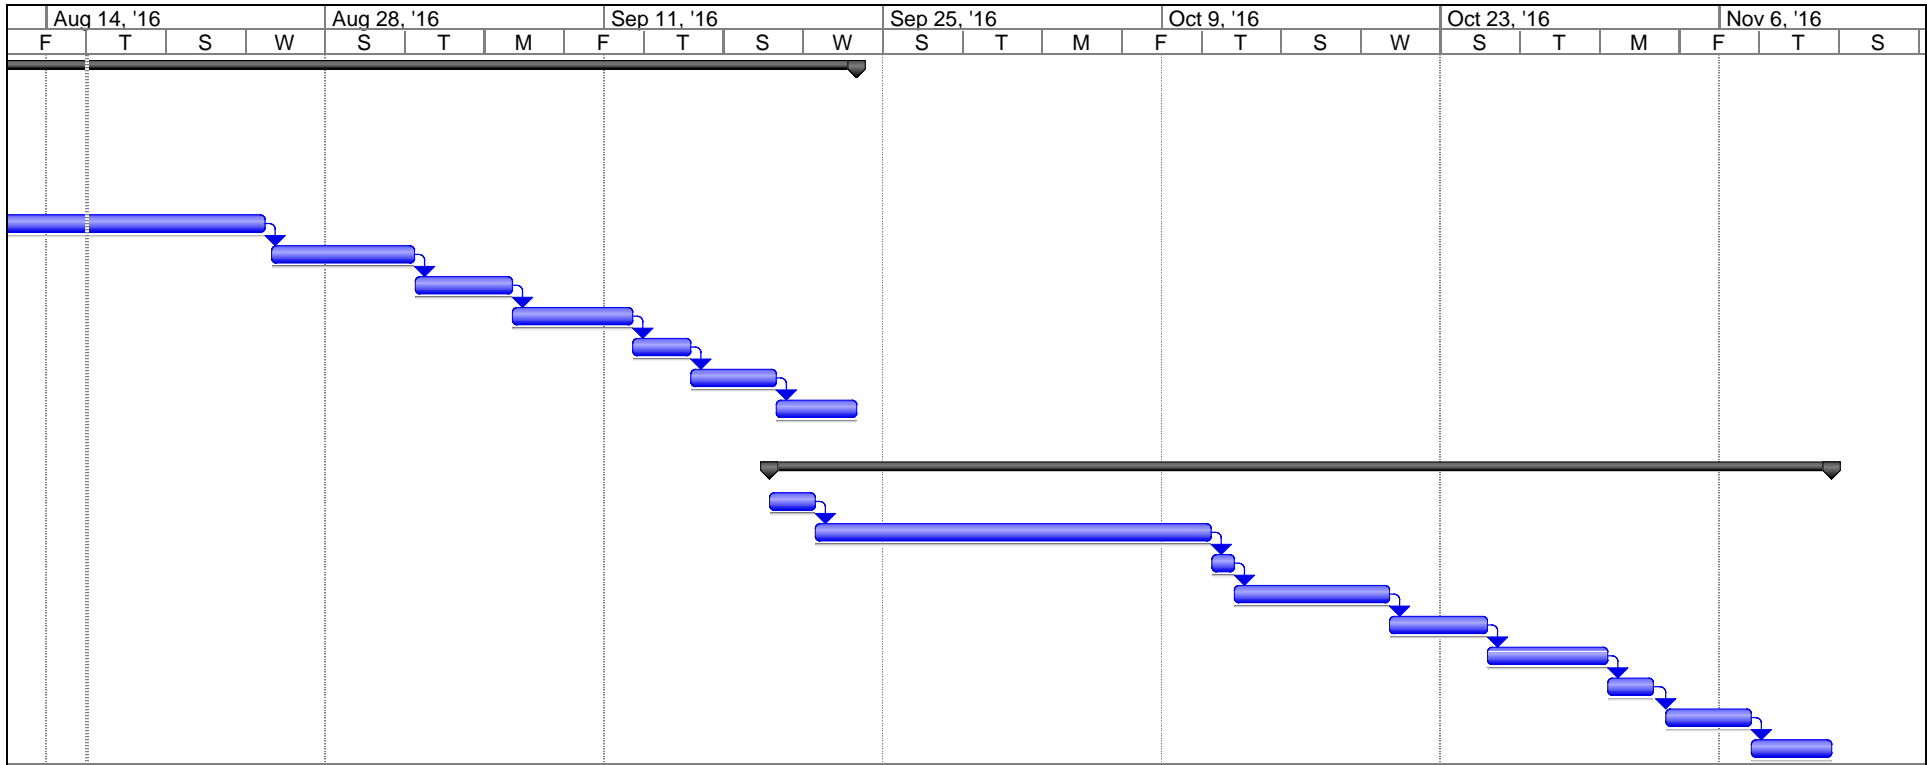

ID	Task Name	Start	Finish	Jun 19, '16				Jul 3, '16			Jul 17, '16				Jul 31, '16			
				F	T	S	W	S	T	M	F	T	S	W	S	T	M	
1	Phase 1	Tue 7/5/16	Fri 9/23/16															
2	Mobilization	Tue 7/5/16	Wed 7/6/16															
3	Pavement Removals	Wed 7/6/16	Mon 7/11/16															
4	Utility Work	Thu 7/14/16	Tue 8/2/16															
5	Pavement Removals	Wed 8/3/16	Thu 8/4/16															
6	EW- Laterals	Thu 8/4/16	Wed 8/24/16															
7	Subgrade Prep/Subbase	Thu 8/25/16	Thu 9/1/16															
8	Trimming/Paving	Thu 9/1/16	Tue 9/6/16															
9	Cure Time	Tue 9/6/16	Mon 9/12/16															
10	Subdrain	Mon 9/12/16	Thu 9/15/16															
11	Driveways	Thu 9/15/16	Mon 9/19/16															
12	Backfill/Restoration	Mon 9/19/16	Fri 9/23/16															
13																		
14	Phase 2	Mon 9/19/16	Fri 11/11/16															
15	Pavement Removals	Mon 9/19/16	Wed 9/21/16															
16	Utility Work	Wed 9/21/16	Tue 10/11/16															
17	Pavement Removals	Tue 10/11/16	Wed 10/12/16															
18	Subgrade Prep/Subbase	Wed 10/12/16	Thu 10/20/16															
19	Trimming/Paving	Thu 10/20/16	Tue 10/25/16															
20	Cure Time	Tue 10/25/16	Mon 10/31/16															
21	Subdrain	Mon 10/31/16	Wed 11/2/16															
22	Driveways	Thu 11/3/16	Mon 11/7/16															
23	Backfill/Restoration	Mon 11/7/16	Fri 11/11/16															



Project: Prelim schedule Date: Tue 8/16/16	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Prelim schedule Date: Tue 8/16/16	Task 	Milestone 	External Tasks 
	Split 	Summary 	External Milestone 
	Progress 	Project Summary 	Deadline 
