



ID	Task Name	Start	Finish	Jun 19, '16				Jul 3, '16			Jul 17, '16				Jul 31, '16		
				F	T	S	W	S	T	M	F	T	S	W	S	T	M
1	Phase 1	Tue 7/5/16	Fri 9/30/16														
2	Mobilization	Tue 7/5/16	Wed 7/6/16														
3	Pavement Removals	Wed 7/6/16	Mon 7/11/16														
4	Utility Work	Thu 7/14/16	Tue 8/2/16														
5	Pavement Removals	Wed 8/3/16	Thu 8/4/16														
6	EW- Laterals	Thu 8/4/16	Wed 8/31/16														
7	Subgrade Prep/Subbase	Thu 9/1/16	Thu 9/8/16														
8	Trimming/Paving	Thu 9/8/16	Tue 9/13/16														
9	Cure Time	Tue 9/13/16	Mon 9/19/16														
10	Subdrain	Mon 9/19/16	Thu 9/22/16														
11	Driveways	Thu 9/22/16	Mon 9/26/16														
12	Backfill/Restoration	Mon 9/26/16	Fri 9/30/16														
13																	
14	Phase 2	Mon 9/19/16	Fri 11/11/16														
15	Pavement Removals	Mon 9/19/16	Wed 9/21/16														
16	Utility Work	Wed 9/21/16	Tue 10/11/16														
17	Pavement Removals	Tue 10/11/16	Wed 10/12/16														
18	Subgrade Prep/Subbase	Wed 10/12/16	Thu 10/20/16														
19	Trimming/Paving	Thu 10/20/16	Tue 10/25/16														
20	Cure Time	Tue 10/25/16	Mon 10/31/16														
21	Subdrain	Mon 10/31/16	Wed 11/2/16														
22	Driveways	Thu 11/3/16	Mon 11/7/16														
23	Backfill/Restoration	Mon 11/7/16	Fri 11/11/16														



Project: Prelim schedule Date: Mon 8/29/16	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

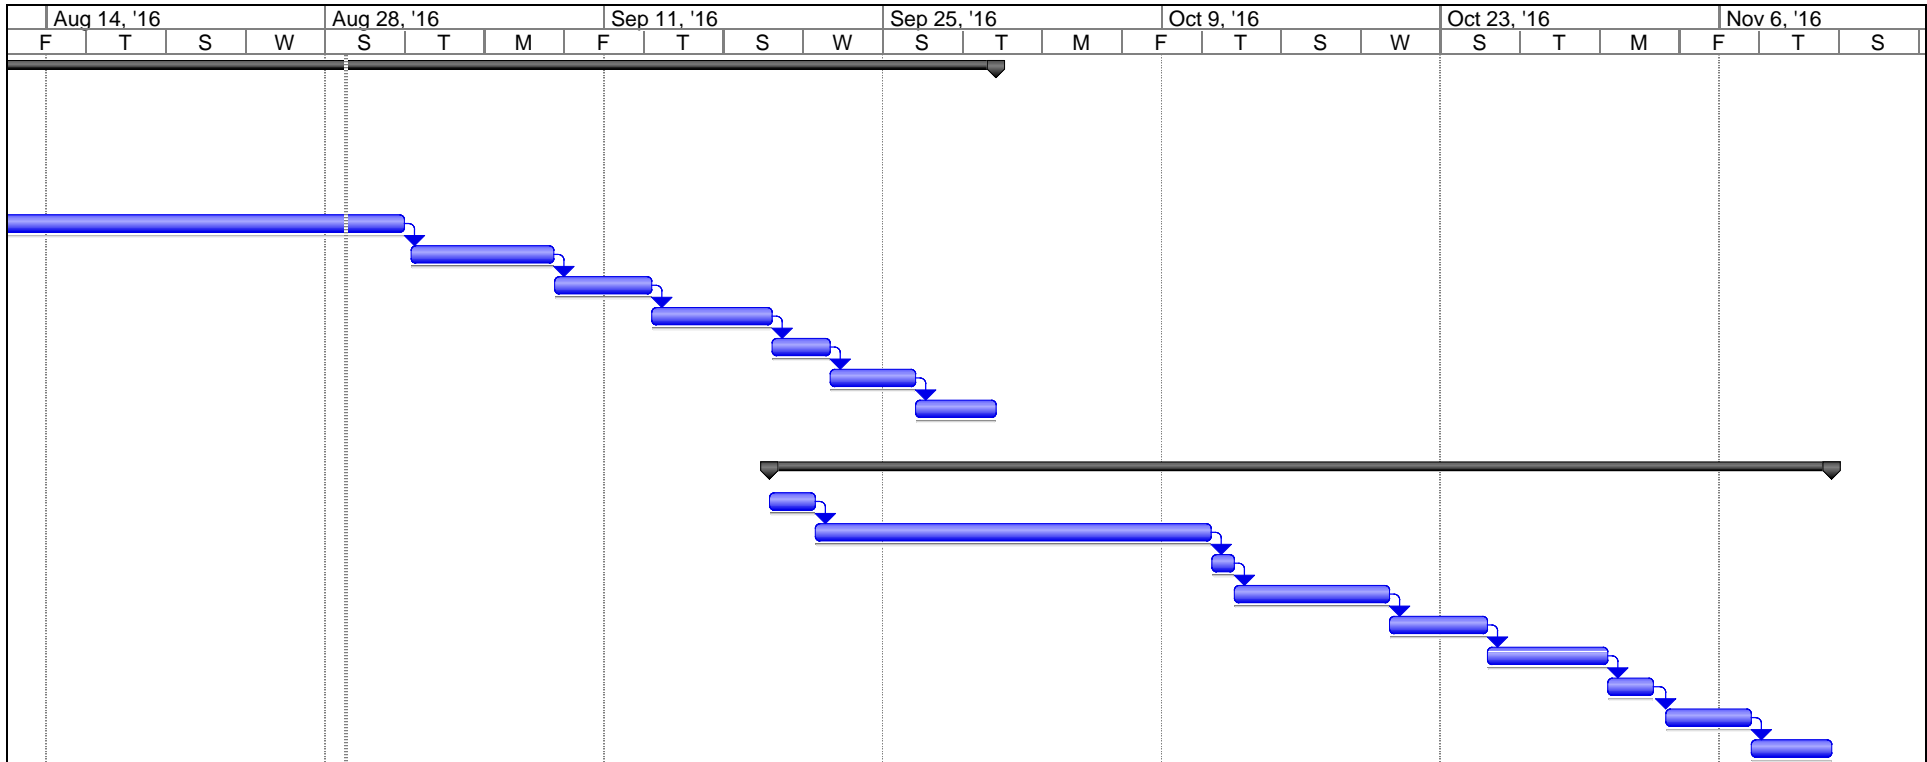

Project: Prelim schedule Date: Mon 8/29/16	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
