








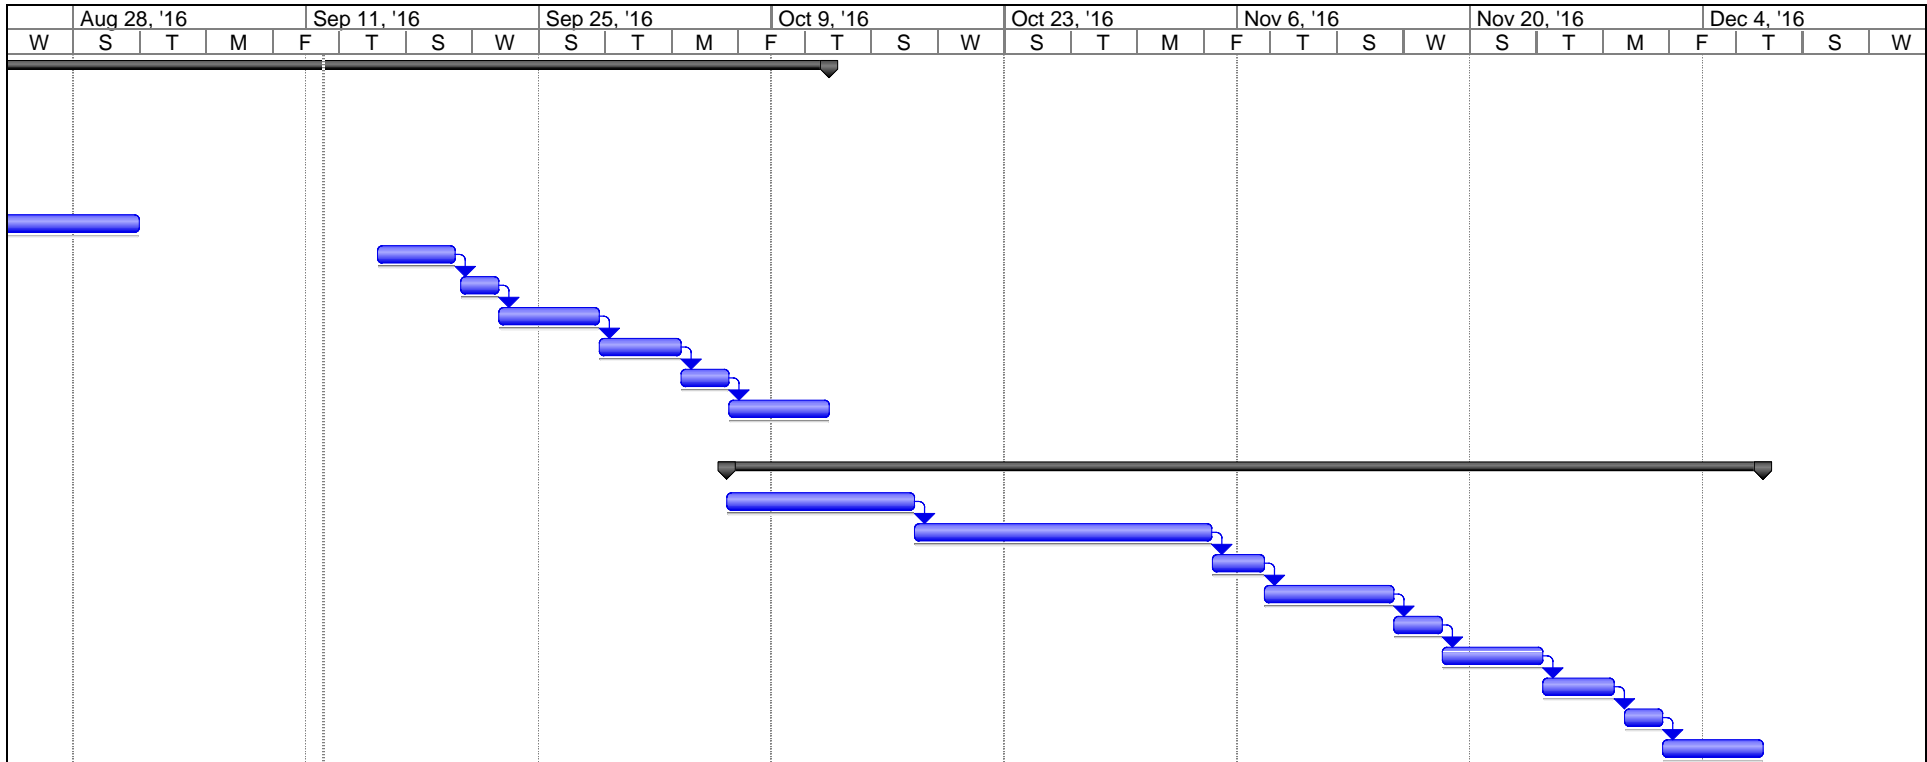










ID	Task Name	Start	Finish	Jun 19, '16				Jul 3, '16				Jul 17, '16				Jul 31, '16				Aug 14, '16		
				F	T	S	W	S	T	M	F	T	S	W	S	T	M	F	T	S		
1	<b>Phase 1</b>	<b>Tue 7/5/16</b>	<b>Wed 10/12/16</b>					▶														
2	Mobilization	Tue 7/5/16	Wed 7/6/16																			
3	Pavement Removals	Wed 7/6/16	Mon 7/11/16																			
4	Utility Work	Thu 7/14/16	Tue 8/2/16																			
5	Pavement Removals	Wed 8/3/16	Thu 8/4/16																			
6	EW- Laterals	Thu 8/4/16	Wed 8/31/16																			
7	Subgrade Prep/Subbase	Thu 9/15/16	Mon 9/19/16																			
8	Trimming/Paving	Tue 9/20/16	Thu 9/22/16																			
9	Cure Time	Thu 9/22/16	Wed 9/28/16																			
10	Subdrain	Wed 9/28/16	Mon 10/3/16																			
11	Driveways	Mon 10/3/16	Thu 10/6/16																			
12	Backfill/Restoration	Thu 10/6/16	Wed 10/12/16																			
13																						
14	<b>Phase 2</b>	<b>Thu 10/6/16</b>	<b>Wed 12/7/16</b>																			
15	Pavement Removals	Thu 10/6/16	Mon 10/17/16																			
16	Utility Work	Mon 10/17/16	Fri 11/4/16																			
17	Pavement Removals	Fri 11/4/16	Mon 11/7/16																			
18	Subgrade Prep/Subbase	Mon 11/7/16	Tue 11/15/16																			
19	Trimming/Paving	Tue 11/15/16	Fri 11/18/16																			
20	Cure Time	Fri 11/18/16	Thu 11/24/16																			
21	Subdrain	Thu 11/24/16	Mon 11/28/16																			
22	Driveways	Tue 11/29/16	Thu 12/1/16																			
23	Backfill/Restoration	Thu 12/1/16	Wed 12/7/16																			

Project: Prelim schedule Date: Mon 9/12/16	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: Prelim schedule Date: Mon 9/12/16	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
